


Combwich Wharf Refurbishment

Update: September 2020

Overview of Main Work Areas

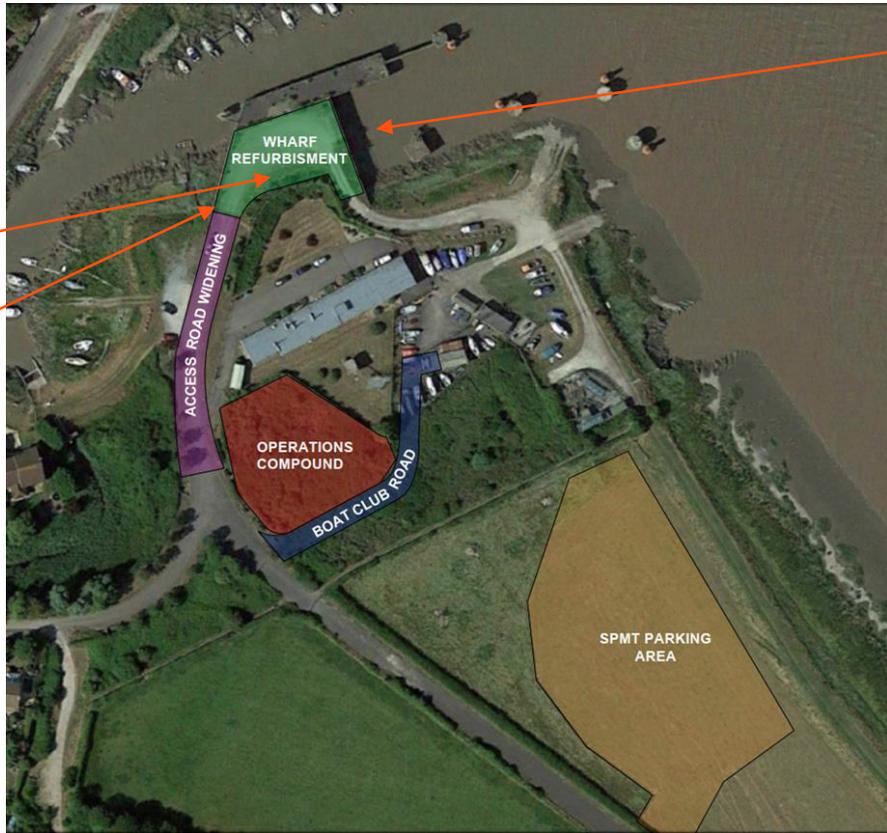

Legato Wall

Abnormal Loads Quay (ALQ)

Acoustic Fencing in place

Progress Update

Our work in September will focus on the removal of the existing Transfer Slab – an important part of the Abnormal Loads Quay which will provide the main area in which parts will be offloaded from the barge.

The existing slab is being removed to allow new piles to be installed, at a greater depth than previous ones. This will provide better support for the replacement Transfer Slab.

We will also be installing a small number of test piles ahead of the main phase of piling in the Autumn.

Over the last few weeks you may have seen padded green fencing surrounding the work area. This is actually an acoustic blanket (image 1), one of the measures in place to help reduce any noise impact.

We've also cut back foliage that was covering the path to the Boat Club pontoon, which will give them better access.

Thank you for your continued patience whilst we complete these works. If you would like to book an appointment to speak with a member of the Community Relations team regarding the refurbishment, please get in touch by telephone on 0333 009 7070 or email us on hinkley-enquiries@edf-energy.com.

